

Project Management Capstone Project

Reduction of Temperature-Sensitive Cargo Misplacement in Warehouse Operations at Jeena & Co.



Project Sponsor

Mr. Puneet Dung
Head of Department – Air Exports (Jeena & Co.)

Team Members



Saransh singh
(25PGDM043)



Mahi Yadav
(25PGDM030)



Chirag
(25PGDM015)



Andeep
(25PGDM008)

CERTIFICATE OF PROJECT APPROVAL

Capstone Project Authorisation - Milestone (part of academic requirements for Project Management T4)

This is to certify that the following project has been presented before the Faculty Guide and is approved for academic submission. The project has been reviewed based on its relevance, feasibility, academic value, and alignment with the course objectives.

PROJECT DETAILS

COMPANY / BRAND SELECTED	JEENA & Co.
PROJECT TITLE	Reduction of Temperature-Sensitive Cargo Misplacement in Warehouse Operations at Jeena & Co. (Delhi Airport Cargo Terminal)
TEAM NUMBER	6 (PMO 2)

TEAM MEMBERS

S.NO.	NAME
1	(25PGDM030) Mahi Yadav
2	(25PGDM008) Andeep
3	(25PGDM043) Saransh Singh
4	(25PGDM015) Chirag

JUSTIFICATION FOR SELECTING THIS PROJECT

S. no	Category	Remarks
1	Value Prop (How does this project contribute to growth, efficiency, customer satisfaction, compliance)	The project aims to reduce storage allocation errors for temperature-sensitive cargo, improving operational accuracy, reducing potential financial losses, and enhancing customer satisfaction through better warehouse handling practices.
2	Resource Availability (Can we acquire budget, talent, time, infra? Will a real stakeholder join the team?)	The project will use the company's existing resources. Guidance from Mr. Puneet Dung, access to warehouse operations, and discussions with warehouse staff will help in collecting information and completing the project.
3	Feasibility (Is this project technically or operationally feasible?)	The project is operationally feasible as it focuses on studying existing warehouse processes and identifying practical improvements that can be implemented within the semester without requiring major infrastructure or technology investments.
4	Risk Assessment (What are the project's financial, operational and legal risks? Can they be mitigated?)	Key risks include limited access to operational data, incomplete historical records, limited staff participation. These risks will be mitigated through management support, process observations, and the use of available records and employee inputs.
5.	Industry Contact Details (Contact person, designation, official phone number/email)	Contact Person: Mr. Puneet Dung Designation: Head of Department – Air Export

FACULTY APPROVAL


PROJECT STATUS

Approved
Revision Required
Approved with Suggestions

This certificate confirms that the above-mentioned project has been reviewed, evaluated, and approved by the Faculty Guide for academic submission.

PROJECT CHARTER					
Project Title	Reduction of Temperature-Sensitive Cargo Misplacement in Warehouse Operations			Project Manager	Mahi Yadav
Project Start Date	8 August 2026	Project End Date	17 September 2026	Project Sponsor	Mr. Puneet Dung (Head of Department – Air Exports)
Business need					
Temperature-sensitive cargo requires storage under specific environmental conditions to maintain product quality and compliance requirements. Incorrect storage allocation can lead to cargo deterioration, customer complaints, financial losses, and operational inefficiencies. This project aims to identify the causes of storage allocation errors and improve warehouse processes to enhance cargo handling accuracy and reduce associated risks.					
Project Scope				Deliverables	
In Scope ➤ Study of the current warehouse process for handling temperature-sensitive cargo. ➤ Analysis of storage allocation procedures. ➤ Identification of causes of storage allocation errors. ➤ Review of existing SOPs and control measures. ➤ Interaction with warehouse personnel and supervisors. ➤ Design and implementing feasible process-control improvements.		Out of Scope ➤ Airline and flight operations. ➤ Construction or expansion of warehouse facilities. ➤ Purchase and implementation of new software or expensive technologies. ➤ Customs clearance activities. ➤ Transportation activities before cargo reaches the warehouse. ➤ Activities after cargo is released from the warehouse.		➤ Current Process Flow Map. ➤ Root Cause Analysis Report. ➤ Review of Existing SOPs and Control Measures. ➤ Proposed Process Improvement Plan. ➤ Implementation Roadmap.	
Risk and Issue → Mitigations				Assumptions / Dependencies	
Risks Limited access to data Limited staff cooperation Incomplete historical data Delay in approval of recommendations Limited semester timeline	Mitigation → Use available records, observations, and supervisor inputs. → Seek support from the warehouse head. → Use current observations and employee feedback. → Focus on practical and feasible recommendations. → Keep the project scope focused and manageable.		➤ Support from the warehouse head and management. ➤ Access to relevant warehouse processes and SOPs. ➤ Availability of required operational data and records. ➤ Cooperation from warehouse staff during data collection. ➤ Permission to observe warehouse operations.		
Financials					
No dedicated project budget is required for the study phase. Financial implications and implementation costs, if any, will be assessed after identifying and evaluating the proposed improvement measures.					
Milestones Schedule					
Milestones			Target Completion Date		Actual Date
M1 – Project Selection Review			9 August 2026		9 August 2026
M2 – Project Initiation Review			9 August 2026		9 August 2026
M3 – Project Planning Review					
M4 – Scheduling & Risk Review					
M5 – Execution & Monitoring Review					
M6 – Final PMO Review					
Project Team			Approval / Review Committee		
(25PGDM030) Mahi Yadav			Project Sponsor	Mr. Puneet Dung (Head of Department – Air Exports)	
(25PGDM015) Chirag			Client	Jeena & Co. (Warehouse Operations)	
(25PGDM043) Saransh Singh			Stakeholders	Mr. Puneet Dung, warehouse staff, supervisors, Jeena management.	
(25PGDM008) Andeep					

M3 WORK BREAKDOWN STRUCTURE

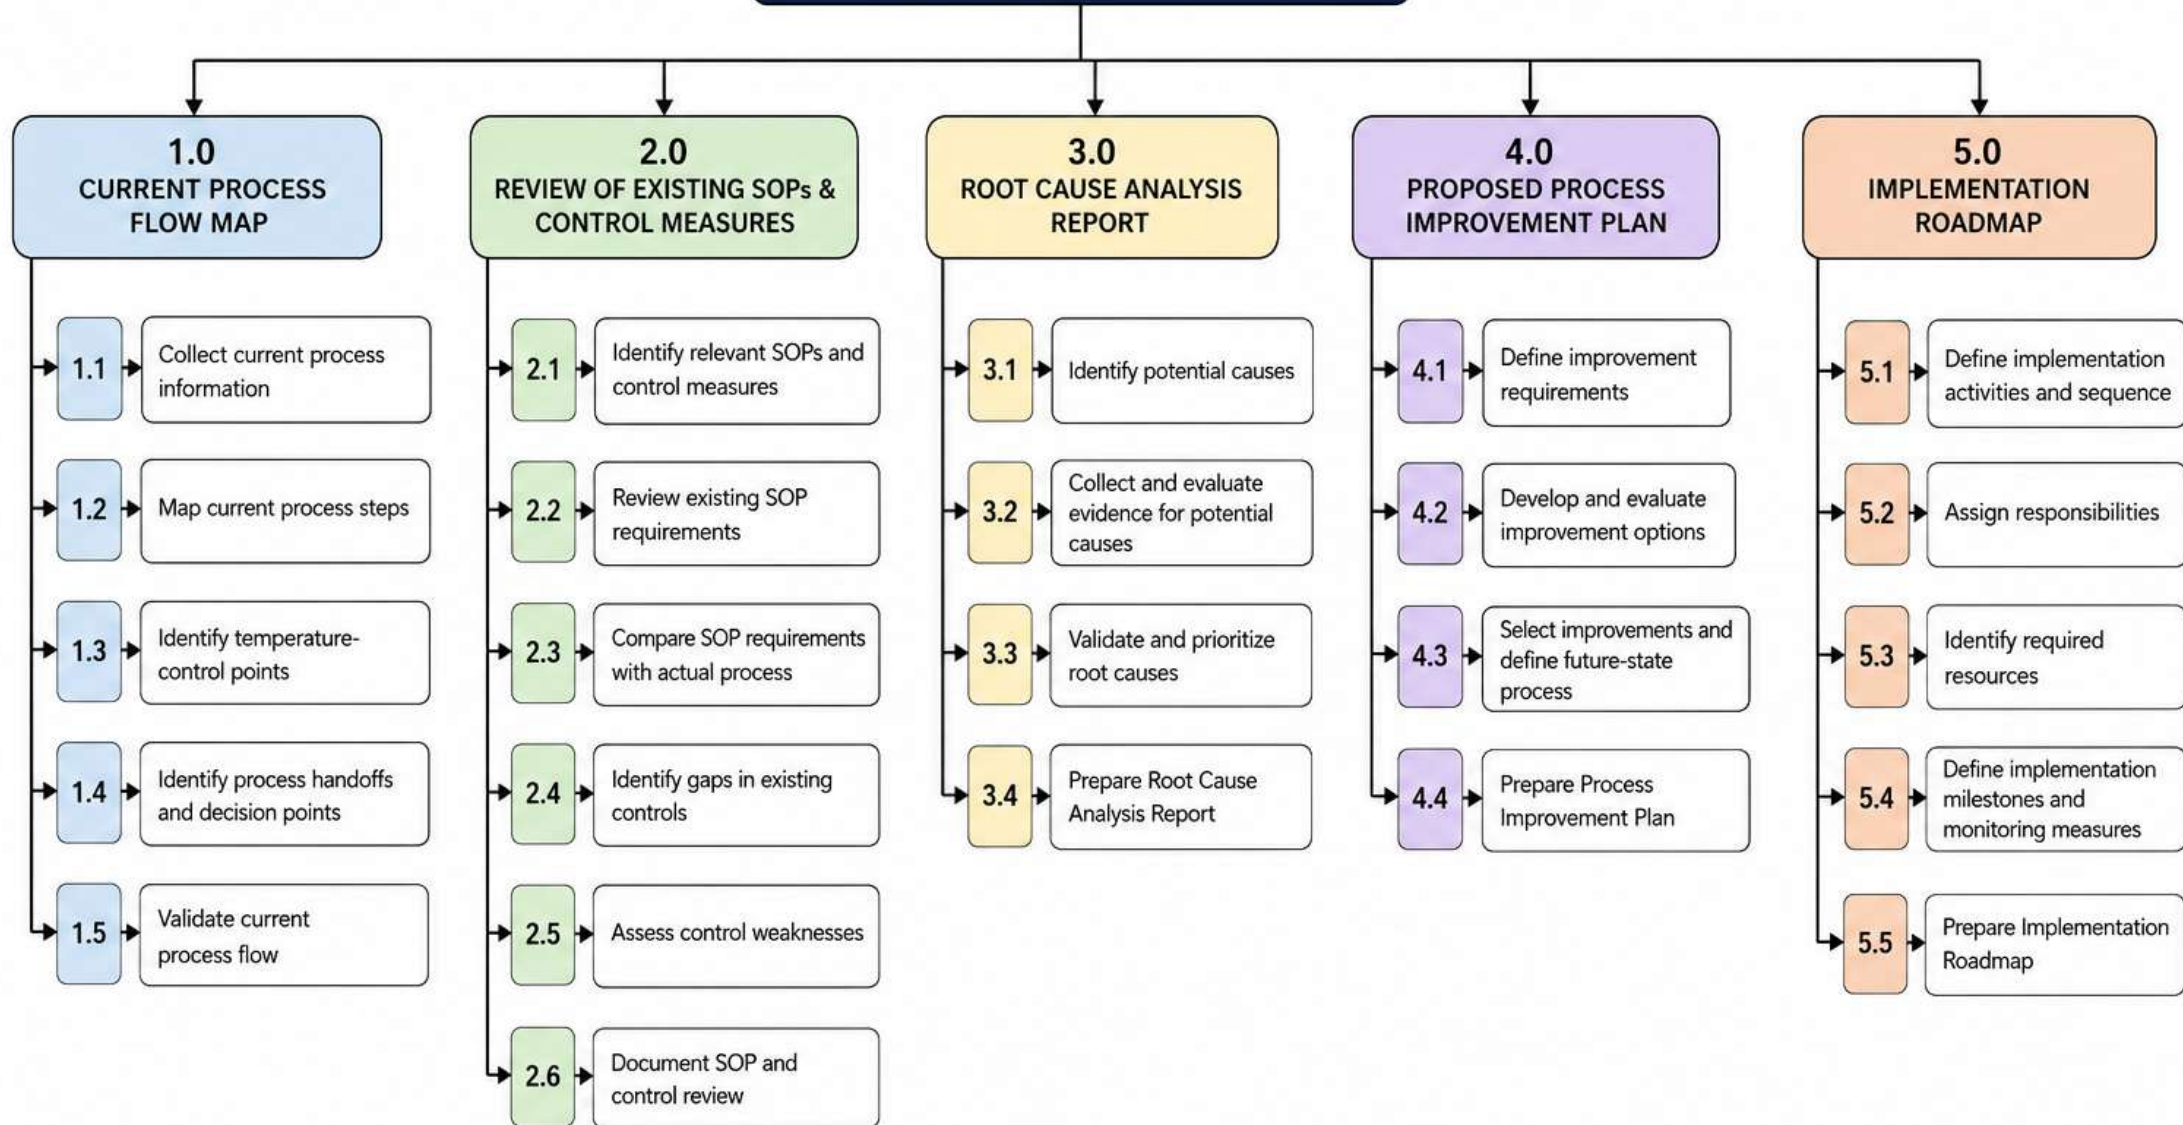


M3 GANTT CHART – 24 TASKS

Project Start: 12 August 2026 | Target Completion: 11 September 2026 | Working Days (Mon–Fri)

[illegible]

JEENA & Co. PROJECT – NETWORK DIAGRAM

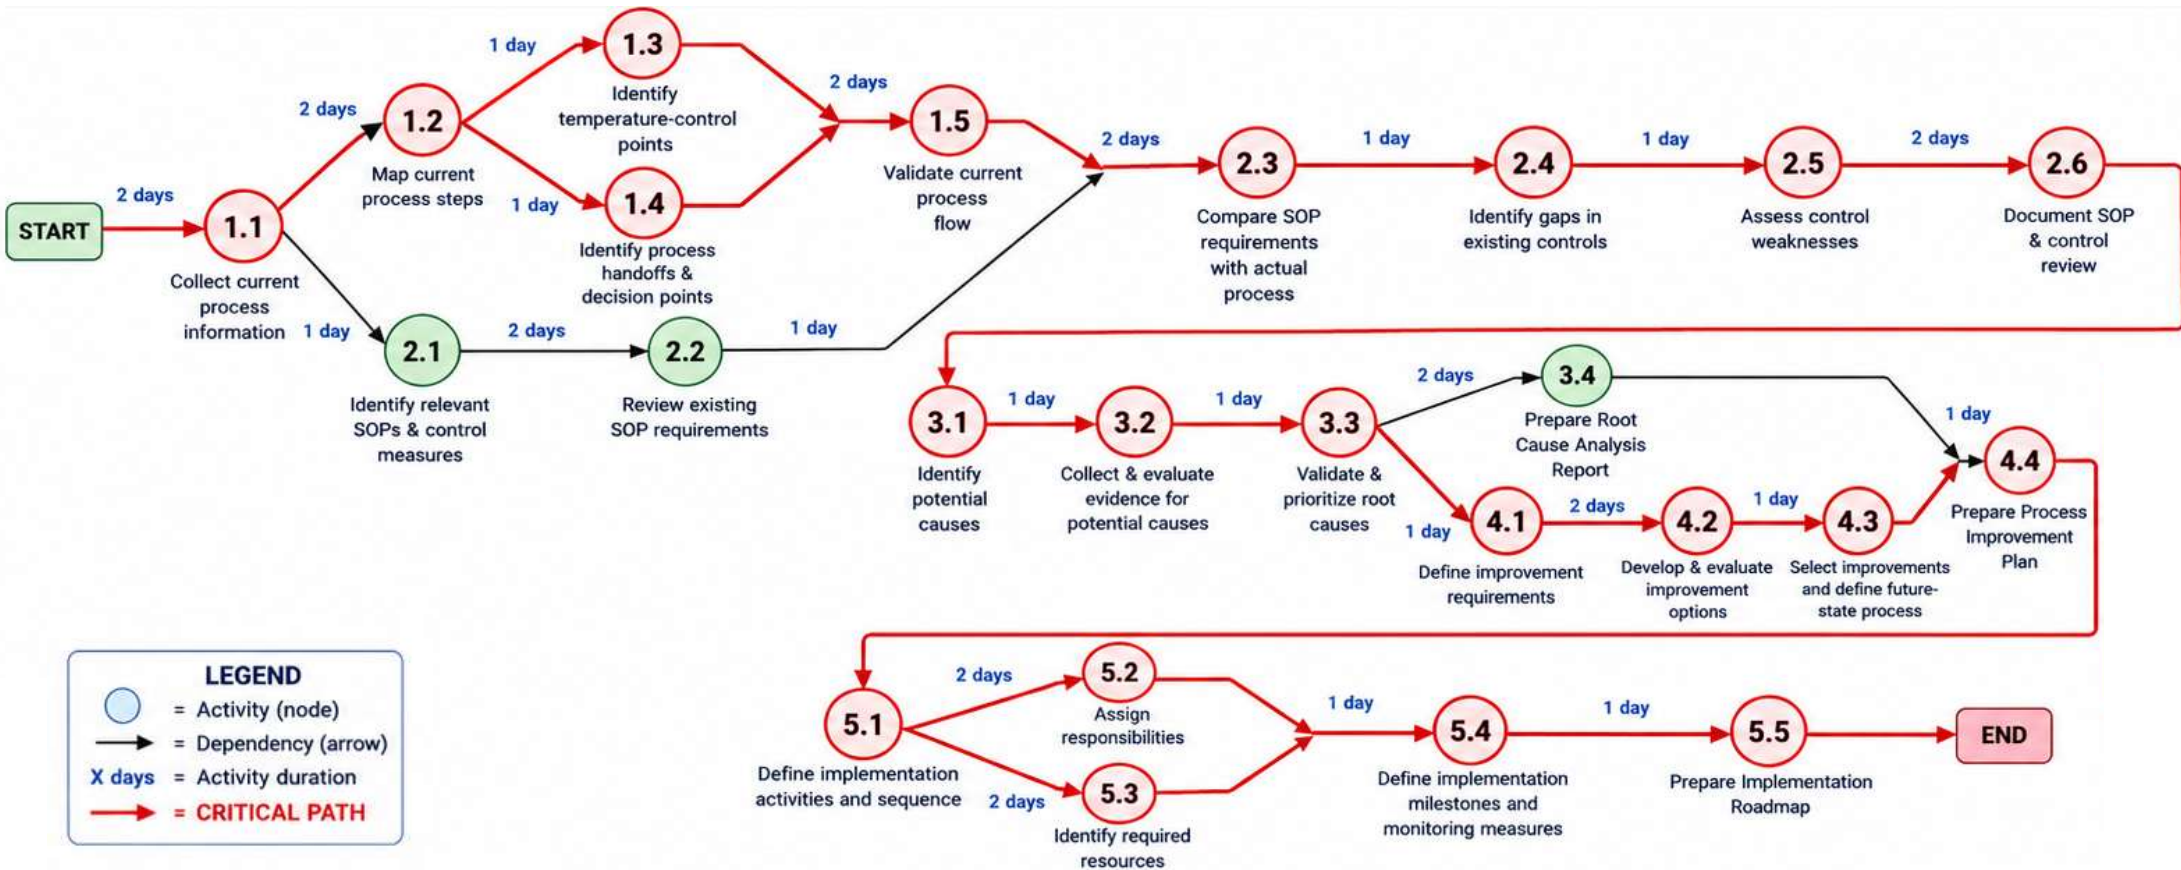

PROJECT PHASES (As per WBS)

**1.0 CURRENT
PROCESS FLOW MAP
(1.1 – 1.5)**

**2.0 REVIEW OF EXISTING
SOPs & CONTROL MEASURES
(2.1 – 2.6)**

**3.0 ROOT CAUSE
ANALYSIS REPORT
(3.1 – 3.4)**

**4.0 PROPOSED PROCESS
IMPROVEMENT PLAN
(4.1 – 4.4)**

**5.0 IMPLEMENTATION
ROADMAP
(5.1 – 5.5)**

JEENA & CO. PROJECT – PROBABILITY-IMPACT MATRIX

Risk Score = Probability × Impact

		IMPACT		
		3 – High	2 – Medium	1 – Low
PROBABILITY	3 – High	9 (High) R1 R4 R9	6 (Medium) R3	3 (Low) –
	2 – Medium	6 (Medium) R2 R5 R7 R8	4 (Medium) R6 R10	2 (Low) –
	1 – Low	3 (Low) –	2 (Low) –	1 (Low) –

RISK LEVEL LEGEND

	7 – 9	High
	4 – 6	Medium
	1 – 3	Low

RISK SUMMARY

High (7 – 9) : R1, R4, R9

Medium (4 – 6) : R2, R3, R5, R6, R7, R8, R10

Low (1 – 3) : None

ID	Risk Description	Probability	Impact	Score	Rating	Mitigation / Response
R1	Limited access to operational data	High (3)	High (3)	9	High	Use available records, observations and supervisor inputs; request data early.
R2	Limited cooperation or availability of warehouse staff	Medium (2)	High (3)	6	Medium	Coordinate observations in advance and seek warehouse-head support.
R3	Incomplete historical data	High (3)	Medium (2)	6	Medium	Supplement historical data with current observations, interviews and available records.
R4	Irregular sponsor availability causing delays in guidance and decisions	High (3)	High (3)	9	High	Schedule meetings in advance and consolidate questions/decisions for each meeting.
R5	Limited project/semester timeline	Medium (2)	High (3)	6	Medium	Prioritize critical activities and monitor the schedule closely.
R6	Mismatch between documented SOPs and actual warehouse practices	Medium (2)	Medium (2)	4	Medium	Compare SOP requirements with observations and staff inputs; validate identified gaps.
R7	Incorrect identification or prioritization of root causes	Medium (2)	High (3)	6	Medium	Cross-check evidence, validate causes with stakeholders and use structured RCA methods.
R8	Proposed process improvements may be impractical or difficult to implement	Medium (2)	High (3)	6	Medium	Evaluate improvements for feasibility, resources, operational impact and practicality.
R9	Delay in validation of project findings by operational stakeholders	High (3)	High (3)	9	High	Request validation early, provide concise findings for review and maintain alternative evidence where possible.
R10	Insufficient or inconsistent operational information from staff or observations	Medium (2)	Medium (2)	4	Medium	Cross-check information from multiple sources and document evidence consistently.

M5 – Change Management

1. Change Scenario → The given change scenario is: “Sponsor unavailable for the next 2 weeks. What will be your response?” The sponsor, Mr. Puneet Dung (Head of Department – Air Exports), is unavailable from 28 August to 11 September 2026.

2. The Situation → The sponsor, Mr. Puneet Dung (Head of Department – Air Exports), is unavailable from 28 August to 11 September 2026. Activities scheduled up to 27 August 2026 have been completed. The change mainly affects activities requiring validation or final decisions. The team must maintain progress while managing the resulting schedule and stakeholder risks.

Key impacts:

- **3.3 – Validate & Prioritize Root Causes:** Final validation affected.
- **4.3 – Select Improvements & Define Future-State Process:** Final decision affected.
- **5.4 – Define Implementation Milestones & Monitoring Measures:** Dependent on final decisions.
- **5.5 – Prepare Implementation Roadmap:** Dependent on the finalized implementation plan.

3. How We Overcome the Situation & Delay (Final Roadmap)

Date	Action
28 Aug – 11 Sep	Prepare preliminary root-cause prioritization using Pareto (80/20) Prepare draft RCA, improvement requirements and improvement options Prepare recommended improvement and proposed future-state process Prepare draft implementation activities, responsibilities and resources
14 Sep	Sponsor returns and validates 3.3 Sponsor reviews the recommended improvement under 4.3 Make any required changes based on sponsor feedback
15 Sep	Finalize 5.4 and 5.5 and close the remaining project work

Original completion: 11 September 2026

Sponsor return: 14 September 2026

Target revised completion: 15 September 2026

Expected overall delay: 4 working days

Recovery / Crashing

A major crash is **not required** in the base recovery plan because most of the analytical and preparatory work will already be completed during the sponsor’s absence. The team will use the prepared outputs to complete validation, revisions, and finalization quickly after the sponsor returns.

If the sponsor requests only minor changes, the team can complete them within **1–2 working days** because the underlying analysis and draft outputs are already prepared.

Final M5 approach: Continue productive work during the sponsor’s absence → prepare evidence-based preliminary outputs → obtain sponsor validation on 14 September → make only necessary revisions → finalize the project by **15 September 2026**.
